
The MSP Redevelopment Commission

MSP Redevelopment Project

Jefferson City, Missouri



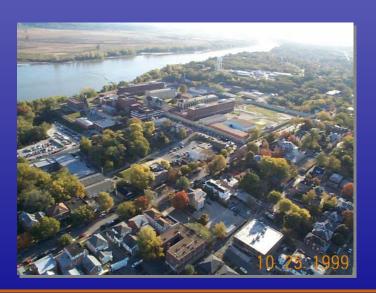

DNR Green Building



DNR Green Building




DNR Green Building




The State of Missouri . Division of Design & Construction


Missouri State Health Lab Building

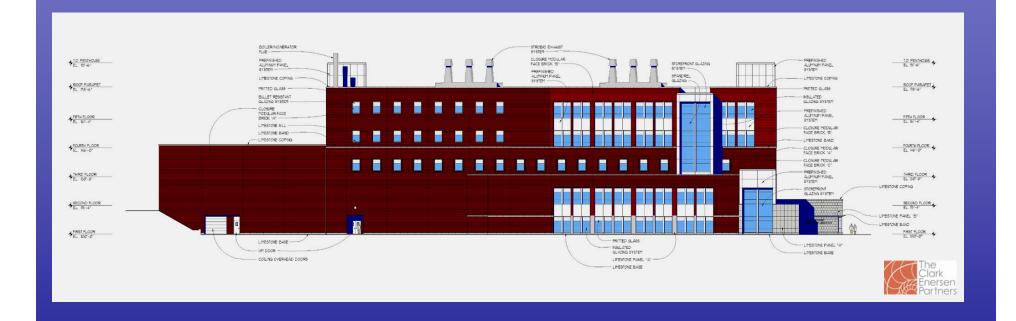

Missouri State Health Lab Building

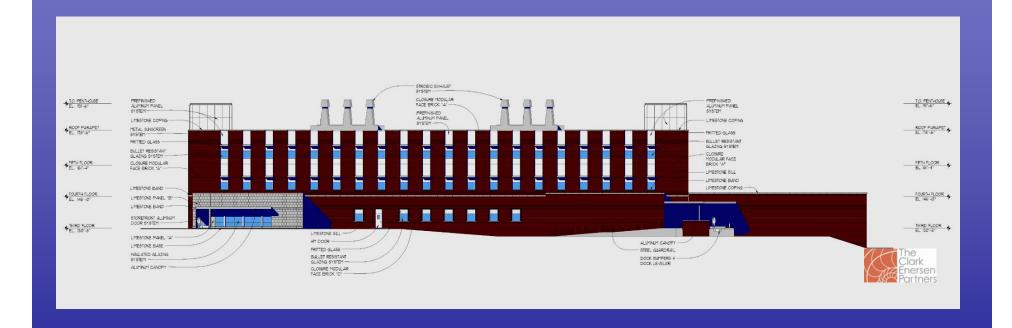

Missouri State Health Lab Building

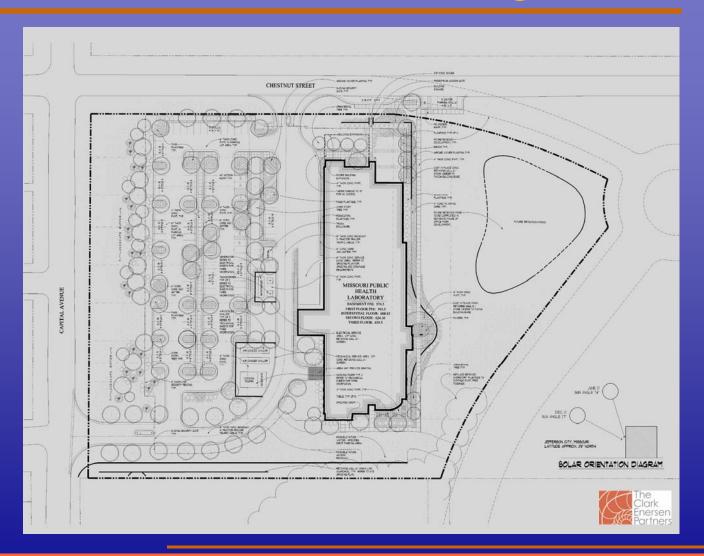

The Master Plan



The State of Missouri . Division of Design & Construction

The Master Plan



The Master Plan



The Next Steps

Planning + Design



Archeological Investigations (Phase I & II)

DNR Site - Completed Health Lab Site Remaining Redevelopment Site

Natural Resource Analysis

Flora & Fauna Threatened & Endangered Species

Historic Designations

Section 106 - Districts, Buildings & The Wall

Environmental Investigations (Phase I & II)

DNR Site - Completed Health Lab Site Remaining Redevelopment Site

The Next Steps

Planning + Design



Decommission Plan for Existing Facility

De-mobilize Existing Infrastructure Demolition Phasing Plan (timeline / strategies) Site & Building Demolition Plan

Demolition Materials Recycling
Wall Stabilization
Caretaker Status (Maintenance & Security)

Infrastructure Redevelopment Plan

Develop Infrastructure Plan Infrastructure Implementation Plan Historic District Heating/Cooling

Site Improvements Plan

On-site Road Plan Parking Plan Grading Plan Landscape Plan

The Next Steps

Planning + Design



Implementation Strategies & Planning

Site & Architectural Design Guidelines
Delivery Systems Guidelines
Design / Build
Lease Purchase
Conventional

Phasing Plan
Facility Interim Use
Public Access

Financial Guidelines & Planning

Project Feasibility
Development Fees
Development Incentives
Funding Sources & Strategies
Revenue Generation Strategies

The Next Steps

Implementation

Decommissioning of MSP Facility - Summer 2004

DOC Move to JCCC

MVE Move to JCCC & Other Locations



MSP Redevelopment Commission Actions

Mothball Buildings to be Retained

Disconnect Other Buildings from Utilities

General Maintenance

Boiler Plant Operation & Utility Services

Grounds keeping

Security

The Next Steps

Implementation Planning



Summer 2004

Construction Projects Underway

DNR Green Building (Completion Fall 2004)

Health Lab (Completion Mid 2005)

Utility Infrastructure Projects

Environmental Abatement Projects

Agencies Occupying Parts of MSP Property

OA Surplus Property

DNR Greenhouse & Grounds keeping

MVE Storage / Warehousing

Questions & Answers




Questions & Answers



Architectural Elements

Buildings Analyzed

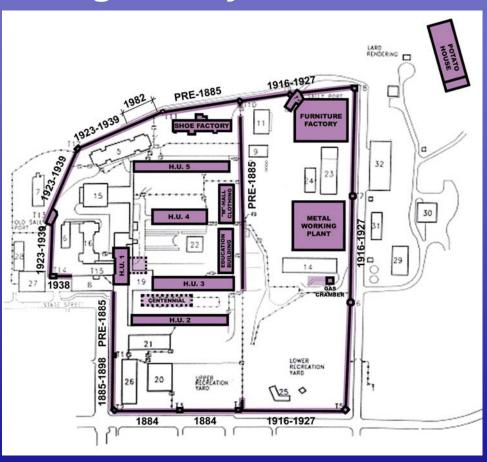

- Housing Unit 1
- Housing Unit 2
- Housing Unit 3
- Housing Unit 4
- Housing Unit 5
- Shoe Factory
- Furniture Factory
- Metal Working Plant
- Centennial Cells
- Gas Chamber
- Potato House
- Education Building & Maintenance Building
- Stone Walls
